GROUND WATER SURVEY REPORT

OPEN WELL/ BOREWELL
DATA OF SURVEY

a) Name of the Party : BBMP

b) Location of the Site : Palanahalli

c) Area of the land : Palanahalli village near Lake.

INVESTIGATION REPORT

1) GEOLOGY OF THE AREA : Gneiss. granitic terrain

2) Recommended Site for drilling : W 5

3) Total depth to be drilled : 900'. 980'

4) Approx. casing pipe required : 90' - 95'

5) No. of water bearing Zones : - 4 -

6) No. of favourable spots marked : - 8 -

7) Qty. of water expected : 2" - 2 1/2"

8) Method of survey carried out : Geo-electrical method.

9) Remarks : 6/12" dia Borewell

HYDROGEOLOGIST
(M.G. RAJASHEKHAR, M.Sc., DEG., F.G.S.)

P.T.O. : Terms & Conditions

BOREWELL SITE PLAN

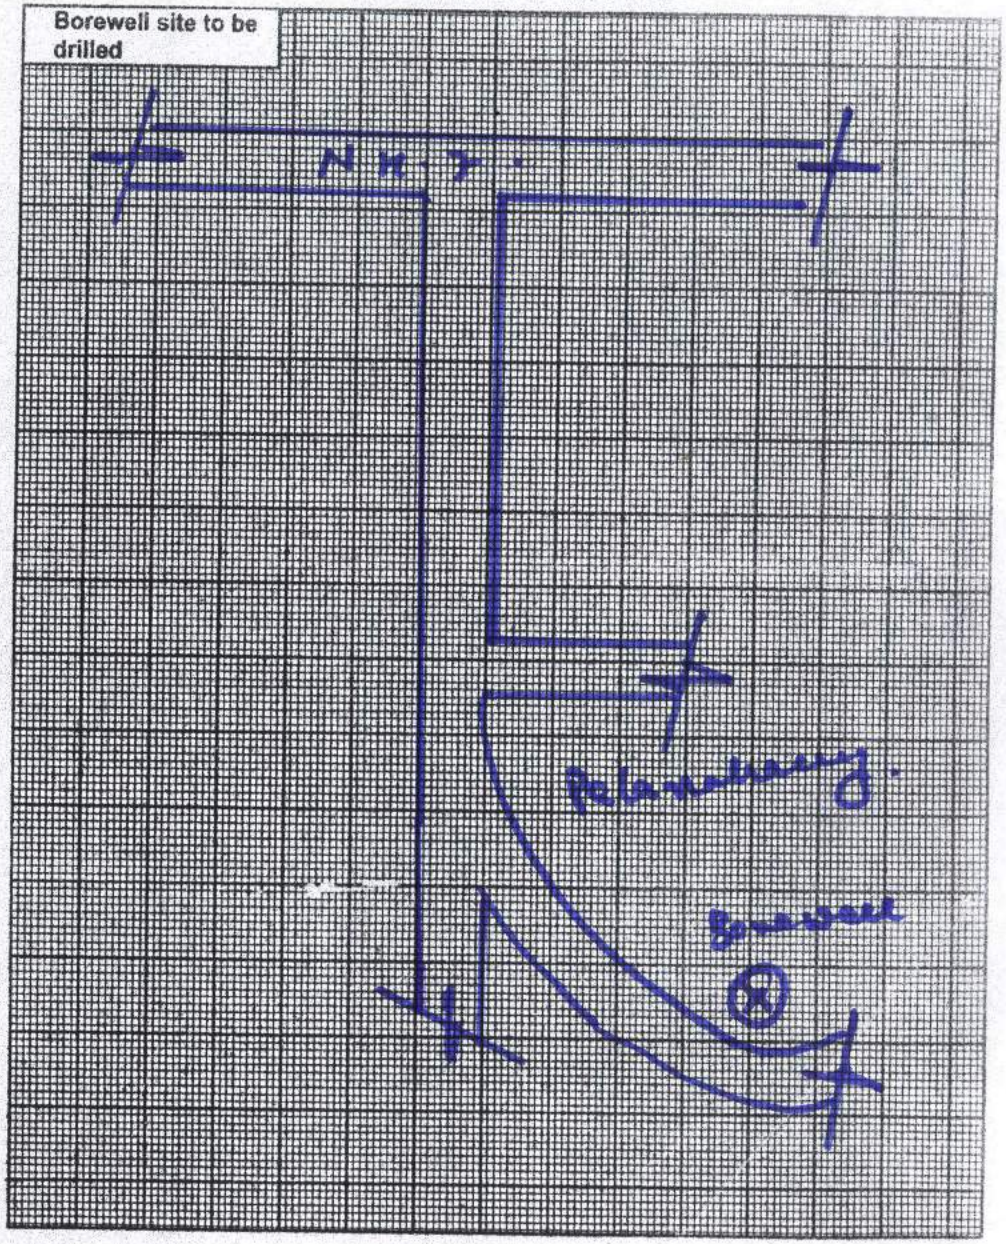

GROUND WATER SURVEY REPORT

OPEN WELL/ BOREWELL
DATA OF SURVEY

a) Name of the Party : AEE. BBMP.

b) Location of the Site : Balaji Enclave

c) Area of the land : Near Dwarkanagar

INVESTIGATION REPORT

1) GEOLOGY OF THE AREA : Gneiss Granite Gneiss

2) Recommended Site for drilling : WS

3) Total depth to be drilled : 1000' - 1100'

4) Approx. casing pipe required : 98' - 108'

5) No. of water bearing Zones : - 4 -

6) No. of favourable spots marked : - 8 -

7) Qty. of water expected : 2 1/2" - 3"

8) Method of survey carried out : Geo-physical method

9) Remarks : 6/12" dia Borewell

HYDROGEOLOGIST
(M.G. RAJASHEKHAR, M.Sc., DEG., F.G.S.)

P.T.O. : Terms & Conditions

BOREWELL SITE PLAN

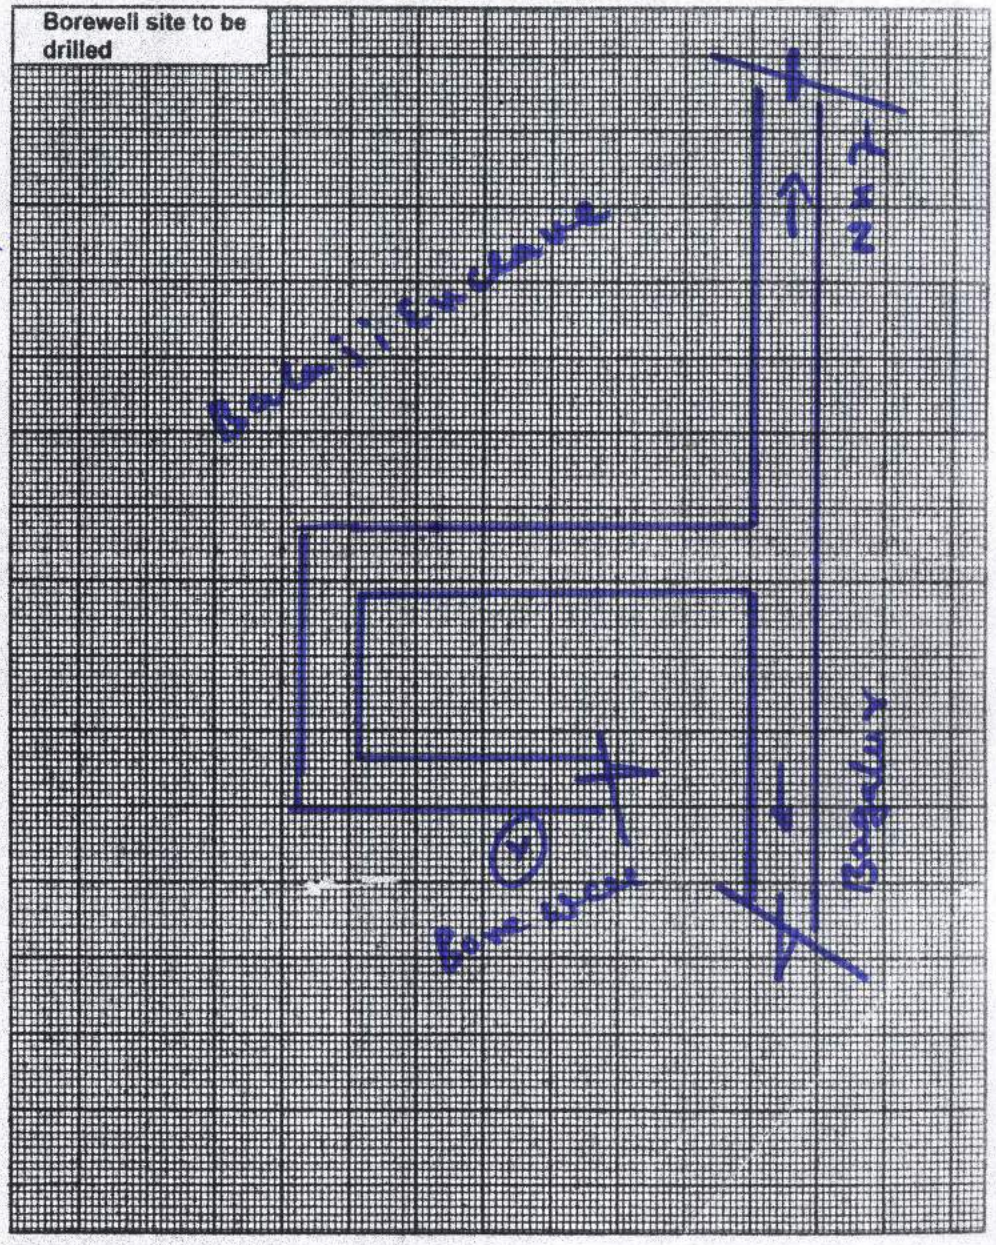

GROUND WATER SURVEY REPORT

OPEN WELL/ BOREWELL
DATA OF SURVEY

a) Name of the Party : BBMP

b) Location of the Site : Cholekanahally Layout

c) Area of the land : Near Venkataramaiah Nayk. Main Road.

INVESTIGATION REPORT

1) GEOLOGY OF THE AREA : Gneiss Granite Gneiss

2) Recommended Site for drilling : W5

3) Total depth to be drilled : 900' - 1000'

4) Approx. casing pipe required : 95' - 105'

5) No. of water bearing Zones : - 4 -

6) No. of favourable spots marked : - 9 -

7) Qty. of water expected : 2" - 2 1/2"

8) Method of survey carried out : Fracture electromagnetic

9) Remarks : 6 1/2" Dia Borewell

HYDROGEOLOGIST
(M.G. RAJASHEKHAR, M.Sc., DEG., F.G.S.)

P.T.O. : Terms & Conditions

BOREWELL SITE PLAN

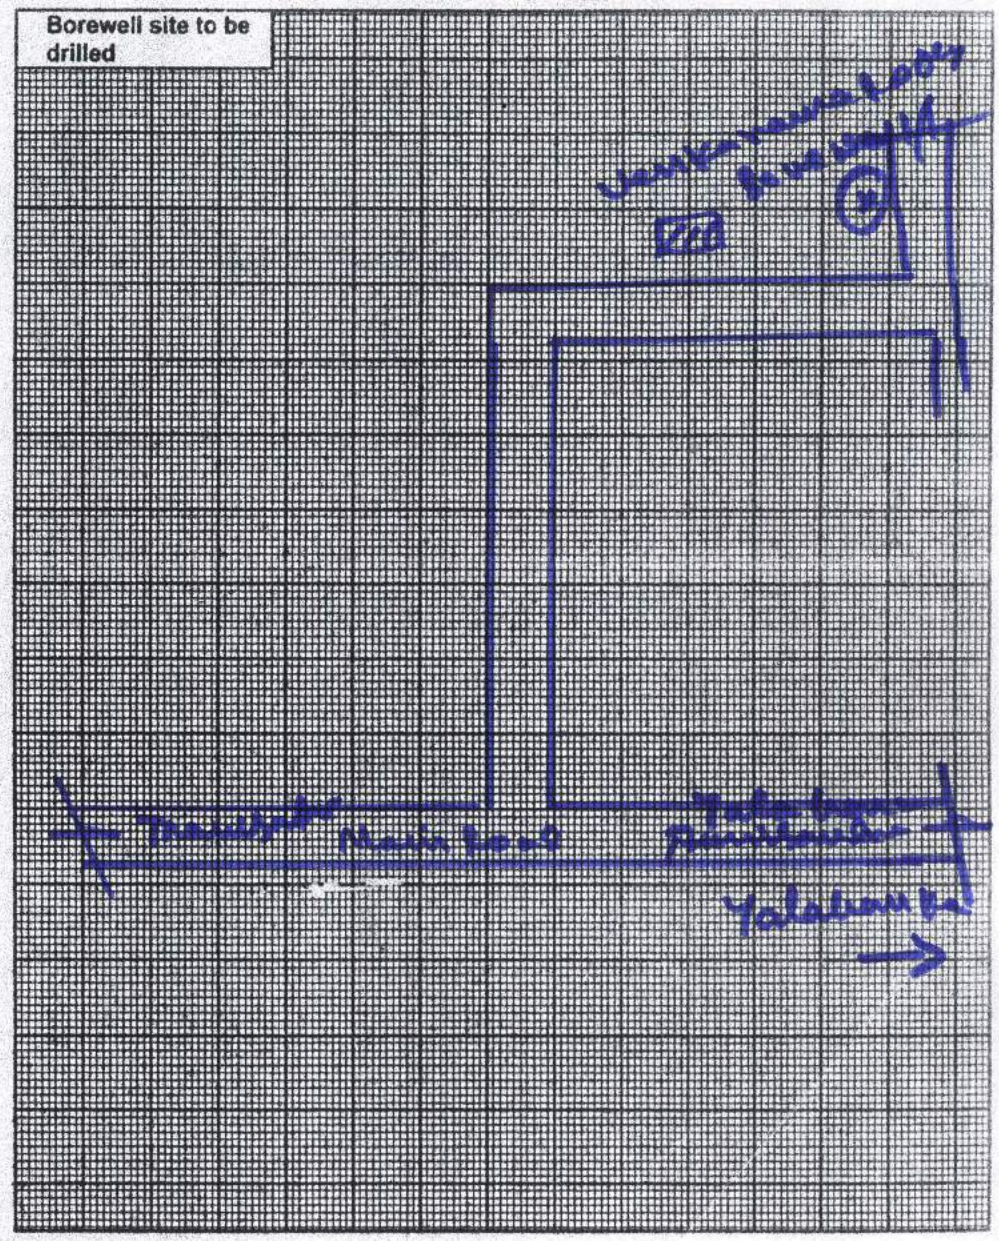

GROUND WATER SURVEY REPORT

OPEN WELL/ BOREWELL
DATA OF SURVEY

a) Name of the Party : AEE. BBMB.

b) Location of the Site : Defence colony.

c) Area of the land : Near Indra Bowli. Dh Main Sukrani

INVESTIGATION REPORT

1) GEOLOGY OF THE AREA : Gneiss Granite Quartz

2) Recommended Site for drilling : W5

3) Total depth to be drilled : 1060' - 1090'

4) Approx. casing pipe required : 97' - 106'

5) No. of water bearing Zones : - 4 -

6) No. of favourable spots marked : - 9 -

7) Qty. of water expected : 2'1/2" - 3"

8) Method of survey carried out : Rota. Percussion Method.

9) Remarks : 6 1/2' Dia Borewell

HYDROGEOLOGIST
(M.G. RAJASHEKHAR, M.Sc., DEG., F.G.S.)

P.T.O. : Terms & Conditions

BOREWELL SITE PLAN

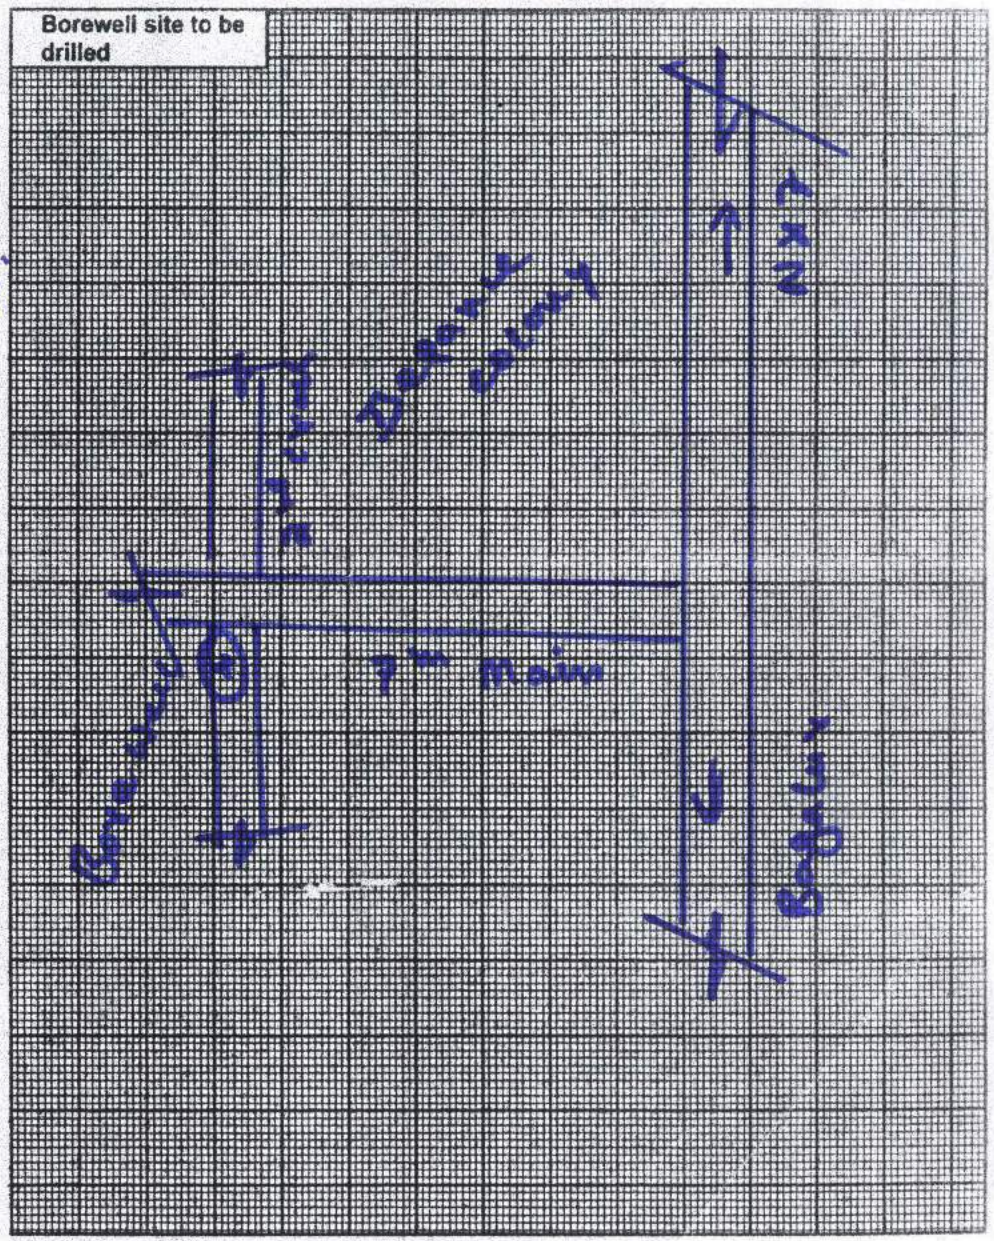

GROUND WATER SURVEY REPORT

OPEN WELL/ BOREWELL
DATA OF SURVEY

a) Name of the Party : AEE. BBMP

b) Location of the Site : Ayappa Badavane

c) Area of the land : Kathigenahalli.

INVESTIGATION REPORT

1) GEOLOGY OF THE AREA : Gneiss Granite Gneiss

2) Recommended Site for drilling : W 5

3) Total depth to be drilled : 1070' - 1090'

4) Approx. casing pipe required : 101' - 109'

5) No. of water bearing Zones : - 4 -

6) No. of favourable spots marked : - 7 -

7) Qty. of water expected : 2" - 2 1/2"

8) Method of survey carried out : Fracture Method

9) Remarks : 8 1/2" dia Borewell.

HYDROGEOLOGIST
(M.G. RAJASHEKHAR, M.Sc., DEG., F.G.S.)

P.T.O. : Terms & Conditions

BOREWELL SITE PLAN

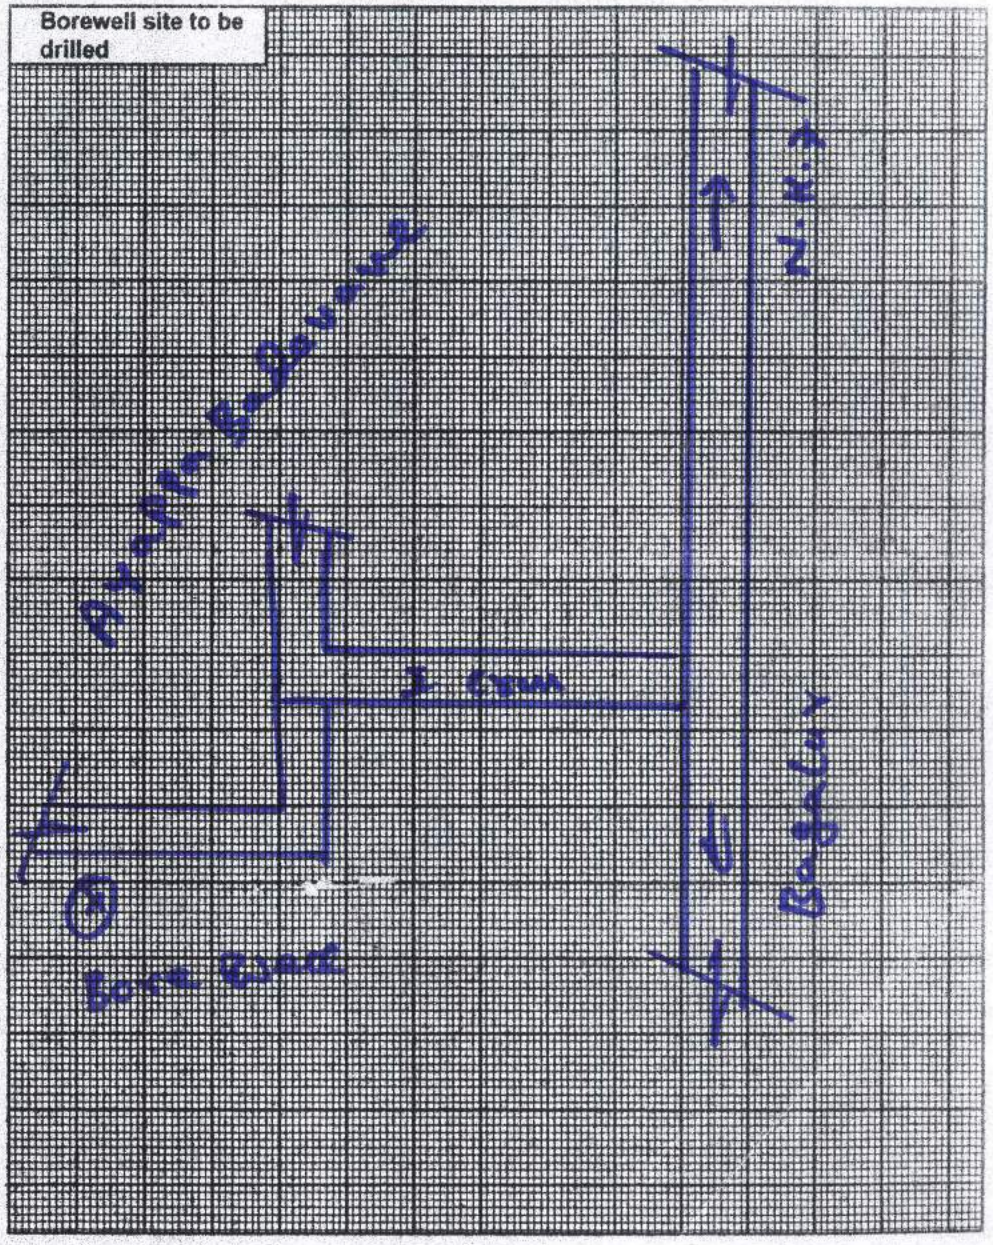

BOREWELL COMPLETION REPORT

VINAYAKA ENTERPRISES

Borewell Drilling Contractors

Mobile : +91 9342202932 / 9343202932

No. 9, Bhadrappa Layout, Bhadrappa Compound, Near Hebbal, Ring Road, Bangalore 560094

No. : 125 Date : 30/10/2016

1. Customer's Name and Address : AEE. BBMP
   with Telephone No. Byatarayanapura Sub Division.
2. Well Location : Palanahalli.
3. Total Well Depth / Drilled in Ft. : 1013 feet.
4. Casing Erected in Ft. : 131 feet
5. Water Struck at the Depth of : 250 feet, 790 feet.
6. Total Yield (Measuring method "V" Norch : 2.00 inches / Inches on "V" Norch)
7. Formation of Soil/Well Water Condition : Boulders/Silt/Loose Soil/Clear Clear
8. At the Depth of : 1013 feet.
9. Recommended to use Jet Pump / Air Compressor / Submersible /Hand Pump Submersible.

The Borewell was drilled in accordance with the company terms and conditions and handed over to customer in good/ satisfied / Party agreed conditions.

Once the well handed over to party, company is no way responsible for further developments if anything in the well or what so ever.

Party's Signature

I, owner of the Well / (Authorised signatory) fully understood the terms and conditions and the well completion report, I also fully understood the quality and quantity of water from the well duly depend upon the nature / formation of ground water and the drilling agency no way responsible for further occurrence / Changes in the bore with full satisfaction. I hereby endorse my signature.

For VINAYAKA ENTERPRISES

Manager / ~~Proprietor~~

Party's Signature

BOREWELL COMPLETION REPORT

VINAYAKA ENTERPRISES

Borewell Drilling Contractors

Mobile : +91 9342202932 / 9343202932

No. 9, Bhadrappa Layout, Bhadrappa Compound, Near Hebbal, Ring Road, Bangalore 560094

No. : 129

Date : 01/11/2016

1. Customer's Name and Address : AEE. BBMP
   with Telephone No. Byatarayanapura Sub Division.
2. Well Location : Chokkanahally Layout.
3. Total Well Depth / Drilled in Ft. : 1004 feet.
4. Casing Erected in Ft. : 148 feet.
5. Water Struck at the Depth of : 310 - 895.
6. Total Yield (Measuring method "V" Norch : 1½ inches / Inches on "V" Norch)
7. Formation of Soil/Well Water Condition : Boulders/Silt/Loose Soil/Clear clear
8. At the Depth of : 1004 feet.
9. Recommended to use Jet Pump / Air Compressor / Submersible /Hand Pump Submersible.

The Borewell was drilled in accordance with the company terms and conditions and handed over to customer in good/ satisfied / Party agreed conditions.

Once the well handed over to party, company is no way responsible for further developments if anything in the well or what so ever.

Party's Signature

I, owner of the Well / (Authorised signatory) fully understood the terms and conditions and the well completion report, I also fully understood the quality and quantity of water from the well duly depend upon the nature / formation of ground water and the drilling agency no way responsible for further occurrence / Changes in the bore with full satisfaction. I hereby endorse my signature.

For VINAYAKA ENTERPRISES

Party's Signature

Manager / Proprietor

BOREWELL COMPLETION REPORT

VINAYAKA ENTERPRISES

Borewell Drilling Contractors

Mobile : +91 9342202932 / 9343202932

No. 9, Bhadrappa Layout, Bhadrappa Compound, Near Hebbal, Ring Road, Bangalore 560094

No. : 128

Date : 3/11/2016

1. Customer's Name and Address : AEE. BBMP

   with Telephone No. Bhatarayanapura Sub Division

2. Well Location : Balaji Enclave.

3. Total Well Depth / Drilled in Ft. : 1011 feet.

4. Casing Erected in Ft. : 138 feet.

5. Water Struck at the Depth of : 318. 720.

6. Total Yield (Measuring method "V" Norch : 3.0 inches / Inches on "V" Norch)

7. Formation of Soil/Well Water Condition : Boulders/Silt/Loose Soil/Clear clear.

8. At the Depth of : 1011 feet.

9. Recommended to use Jet Pump / Air Compressor / Submersible /Hand Pump Submersible.

The Borewell was drilled in accordance with the company terms and conditions and handed over to customer in good/ satisfied / Party agreed conditions.

Once the well handed over to party, company is no way responsible for further developments if anything in the well or what so ever.

Party's Signature

I, owner of the Well / (Authorised signatory) fully understood the terms and conditions and the well completion report, I also fully understood the quality and quantity of water from the well duly depend upon the nature / formation of ground water and the drilling agency no way responsible for further occurrence / Changes in the bore with full satisfaction. I hereby endorse my signature.

For VINAYAKA ENTERPRISES

Manager / ~~Proprietor~~

Party's Signature

BOREWELL COMPLETION REPORT

VINAYAKA ENTERPRISES

Borewell Drilling Contractors

Mobile : +91 9342202932 / 9343202932

No. 9, Bhadrappa Layout, Bhadrappa Compound, Near Hebbal, Ring Road, Bangalore 560094

No. : 127

Date : 5/11/2016

1. Customer's Name and Address : AEE. BBMP

with Telephone No. Byatarayanapura Subdivision.

2. Well Location : Defence Colony.

3. Total Well Depth / Drilled in Ft. : 1007 feet.

4. Casing Erected in Ft. : 171 feet.

5. Water Struck at the Depth of : 370 - 815.

6. Total Yield (Measuring method "V" Norch : 2.0 inches / Inches on "V" Norch)

7. Formation of Soil/Well Water Condition : Boulders/Silt/Loose Soil/Clear Clear.

8. At the Depth of : 1007 feet.

9. Recommended to use Jet Pump / Air Compressor / Submersible /Hand Pump Submersible

The Borewell was drilled in accordance with the company terms and conditions and handed over to customer in good/ satisfied / Party agreed conditions.

Once the well handed over to party, company is no way responsible for further developments if anything in the well or what so ever.

Party's Signature

I, owner of the Well / (Authorised signatory) fully understood the terms and conditions and the well completion report, I also fully understood the quality and quantity of water from the well duly depend upon the nature / formation of ground water and the drilling agency no way responsible for further occurrence / Changes in the bore with full satisfaction. I hereby endorse my signature.

For VINAYAKA ENTERPRISES

Manager / ~~Proprietor~~

Party's Signature

BOREWELL COMPLETION REPORT

VINAYAKA ENTERPRISES

Borewell Drilling Contractors

Mobile : +91 9342202932 / 9343202932

No. 9, Bhadrappa Layout, Bhadrappa Compound, Near Hebbal, Ring Road, Bangalore 560094

No. : 126 Date : 7/11/2016

1. Customer's Name and Address : AEE. BBMP
   with Telephone No. Byatarayanapura Sub division.
2. Well Location : Ayappa Badavane.
3. Total Well Depth / Drilled in Ft. : 1051 feet.
4. Casing Erected in Ft. : 151 feet
5. Water Struck at the Depth of : 347. 782
6. Total Yield (Measuring method "V" Norch : 2.0 inches. / Inches on "V" Norch)
7. Formation of Soil/Well Water Condition : Boulders/Silt/Loose Soil/Clear Clear
8. At the Depth of : 1051 feet.
9. Recommended to use Jet Pump / Air Compressor / Submersible /Hand Pump Submersible.

The Borewell was drilled in accordance with the company terms and conditions and handed over to customer in good/ satisfied / Party agreed conditions.

Once the well handed over to party, company is no way responsible for further developments if anything in the well or what so ever.

Party's Signature

I, owner of the Well / (Authorised signatory) fully understood the terms and conditions and the well completion report, I also fully understood the quality and quantity of water from the well duly depend upon the nature / formation of ground water and the drilling agency no way responsible for further occurrence / Changes in the bore with full satisfaction. I hereby endorse my signature.

For VINAYAKA ENTERPRISES

Party's Signature

Manager / ~~Proprietor~~
